

Jira Lab 2

Pharmacy Expiry & Re-order Dispatch Engine

Name: Debargho Banerji

SRN: PES1UG24CS141

Required Jira Screenshots

SS1 – Epic and User Stories

Epic with its associated User Stories and Story Points.

The screenshot displays the Jira interface for a team named 'My Software Team'. The left sidebar shows navigation options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', 'Starred', 'Recent', 'My Software Team', 'More spaces', 'Recommended', 'Create a roadmap', 'Filters', 'Dashboards', 'Teams', 'Goals', 'Projects', and 'Customize sidebar'. The main area shows a Kanban board with a list of tasks. The tasks are organized into columns: 'Work', 'Assignee', 'Reporter', 'Priority', 'Status', and 'Rt'. The tasks are as follows:

Task ID	Task Name	Assignee	Reporter	Priority	Status	Rt
KAN-2	Task 2	Unassigned	DEBARGHO BA...	None	Done	Done
KAN-3	Subtask 2.1	Unassigned	DEBARGHO BA...	None	To Do	Unresolv
KAN-4	Batch & Expiry Management	Unassigned	DEBARGHO BA...	Medium	To Do	Unresolv
KAN-7	Maintain Medicine Batch Records	Unassigned	DEBARGHO BA...	High	Done	Done
KAN-8	Identify Expired Medicine Batches	Unassigned	DEBARGHO BA...	High	Done	Done
KAN-5	FEFO Dispensing	Unassigned	DEBARGHO BA...	Medium	To Do	Unresolv
KAN-9	Enforce FEFO Picking Order	Unassigned	DEBARGHO BA...	High	Done	Done
KAN-10	Generate FEFO Dispensing List	Unassigned	DEBARGHO BA...	High	Done	Done
KAN-6	Automated Stock Re-order	Unassigned	DEBARGHO BA...	Medium	To Do	Unresolv
KAN-11	Automated Stock Re-order	Unassigned	DEBARGHO BA...	High	Done	Done

The bottom of the screen shows a '+ Create' button and a page indicator '6 of 6'.

SS2 – Backlog and Story Point Assignments

Backlog showing Sprint 1 and Sprint 2 with Story Point values.

☐ **KAN Sprint 1** 7 Sep – 20 Sep (3 work items) 13 0 0 Start sprint ...

Complete the core medicine inventory management tasks, including batch and expiry tracking, FEFO dispensing, and automated stock re-ordering.

☐ **KAN-7** Maintain Medicine Batch Records Batch & E... To Do 5 ^ 👤

☐ **KAN-8** Identify Expired Medicine Batches Batch & E... To Do 3 ^ 👤 ...

☐ **KAN-9** Enforce FEFO Picking Order FEFO Dis... To Do 5 ^ 👤

+ Create

☐ **KAN Sprint 2** 21 Sep – 4 Oct (2 work items) 13 0 0 Start sprint ...

Complete FEFO dispensing generation and automate medicine stock re-ordering.

☐ **KAN-10** Generate FEFO Dispensi... FEFO Dispensing To Do 5 ^ 👤

☐ **KAN-11** Automated Stock Re-order Automated Stock R... To Do 8 ^ 👤

+ Create

SS3 – Active Sprint (To Do)

Active Sprint board showing the five Sprint 1 stories in To Do.

To Do 3



Maintain Medicine Batch Records

Parent

 Batch & Expiry Management ▾

 KAN-7

5



Identify Expired Medicine Batches

Parent

+ Create

To Do3

Identify Expired Medicine Batches

Parent

Batch & Expiry Management

KAN-83

Enforce FEFO Picking Order

Parent

+ Create

In Progress0

+ Create

In Review0

+ Create

Done

+ Cre

To Do3

Parent

Batch & Expiry Management

KAN-83

Enforce FEFO Picking Order

Parent

FEFO Dispensing

KAN-95

+ Create

In Progress0

+ Create

In Review0

+ Create

Done

+ Cre

Spaces

My Software Team

...

Summary

List

Board

Development

Forms

Timeline

Docs

Backlog

+

Search board

DB

Filter

Group

Complete sprint

To Do2

Generate FEFO Dispensing List

Parent

FEFO Dispensing

KAN-10

5

Automated Stock Re-order

Parent

Automated Stock Re-order

KAN-11

8

+ Create

In Progress0

+ Create

In Review0

+ Create


Done0

+ Create


+

SS4 – Active Sprint (Done)

Active Sprint board showing the five Sprint 1 stories completed in Done.

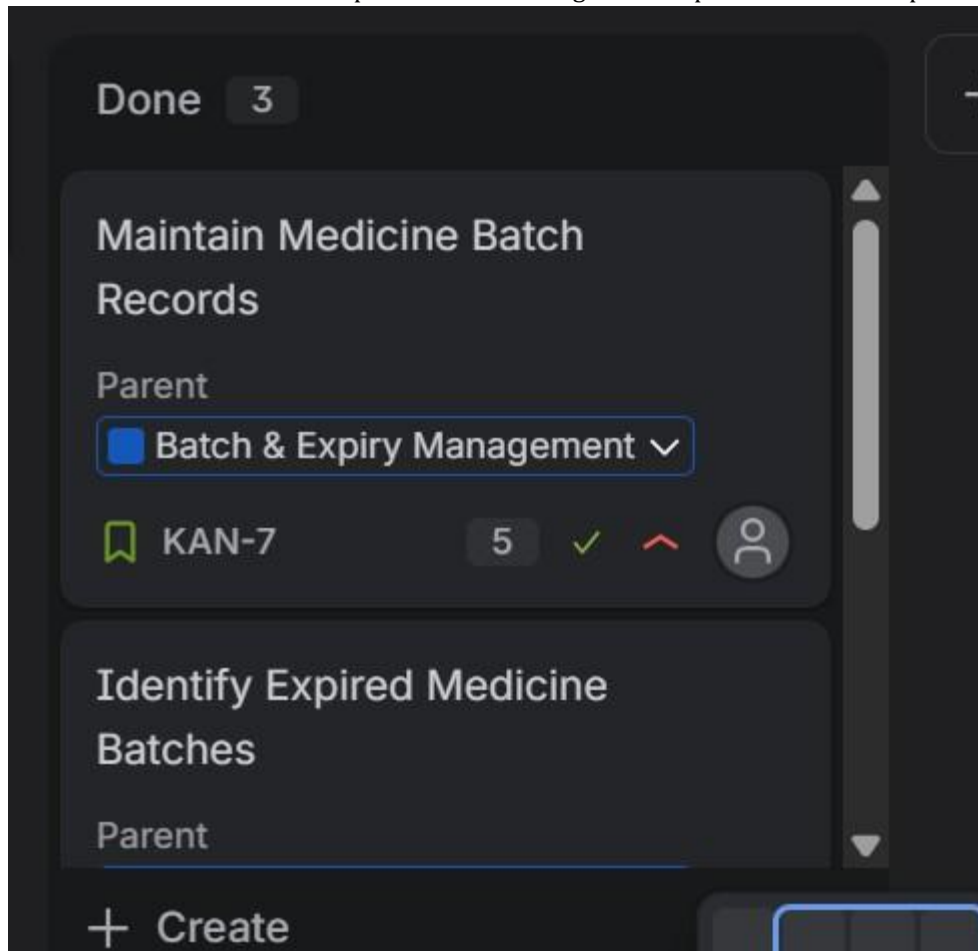

Done 3



Parent

☒ Batch & Expiry Management ▾

KAN-8

3



Enforce FEFO Picking
Order

Parent

☒ FEFO Dispensing ▾

KAN-9

5



+ Create

Jira

Search

Create

See plans

DB

For you

Recent

Starred

Apps

Plans

Spaces

Starred

(Example) Billing System Dev

Recent

My Software Team

More spaces

Recommended

Create a roadmap

Try

Filters

Dashboards

Teams

Goals

Projects

Customize sidebar

Spaces

My Software Team

Summary

List

Board

Development

Forms

Timeline

Docs

Backlog

Search board

DB

Filter

Group

Complete sprint

To Do

0

Create

In Progress

0

Create

In Review

0

Create

Done

2

Generate FEFO Dispensing List

Parent

FEFO Dispensing

KAN-10

5

Automated Stock Re-order

Parent

Automated Stock Re-order

KAN-11

8

Create

SS5 – Burndown Chart

Sprint 1 Burndown Chart :



Reflection & Analysis

1. Did your estimations reflect the actual effort?

Answer:

Yes, in the sense expected for a simulation. KAN-10 (Generate FEFO Dispensing List) was estimated at 5 story points and KAN-11 (Automated Stock Re-order) at 8 story points. This split reflects that the re-order logic — checking stock against a safety threshold, avoiding duplicate purchase-order requests, and dispatching to the supplier — carries more complexity and uncertainty than generating a batch-ordered dispensing list. Both stories were completed within Sprint 2, so the estimates proved workable in practice. Since this was a simulated sprint with no real development time behind it, the points should be read as relative measures of effort and complexity rather than as a measurement of actual hours spent.

2. Was your backlog well-prioritized?

Answer:

Yes. Both KAN-10 and KAN-11 were assigned High priority, and this correctly mirrors their source requirements: KAN-10 traces to FR-001/FR-004 (FEFO picking order and dispensing list generation), and KAN-11 traces to FR-005 (automatic purchase order generation on low stock). These are the two functional requirements most central to the system's core purpose — preventing expired medicines from being dispensed and preventing stock-outs — so pulling them into the sprint ahead of lower-priority, non-functional work (such as response-time or encryption tuning under NFR-001/NFR-002) was the right call for a structured, sprint-ready backlog.

3. How did your simulated sprint align with your plan?

Answer:

The simulated sprint aligned closely with the plan. KAN-10 and KAN-11 were selected for Sprint 2, placed on the Active Sprint board, and moved through the full workflow — To Do → In Progress → In Review → Done. The sprint closed with both stories completed, delivering all 13 of the 13 planned story points, exactly as intended in sprint planning.

4. What insights did the burndown chart give about your team's capacity?

Answer:

The burndown chart showed the sprint's remaining work trending down from 13 story points to 0 as KAN-10 and KAN-11 were completed, indicating that the planned Sprint 2 workload was fully delivered within the simulated sprint window. This suggests the team's demonstrated capacity for this scope was about 13 story points. Because this was a simulation covering a single sprint, more real sprint data would be needed to establish a reliable long-term team velocity rather than a one-off capacity figure.

Acknowledgments:

Several external resources, including technical documentation, online references, and AI-assisted resources, were consulted to support the understanding and development of this project/lab-work
